


# I-DIAGRAMME OF MADHYA GANGA CANAL CONSTRUCTION DIVISION-5, BIJNOR (Stage-II)

From Km. 0.000 to Km. 0.350 and Km. 12.000 to Km. 14.040 (2015-16)

Progress up to 31.03.2016

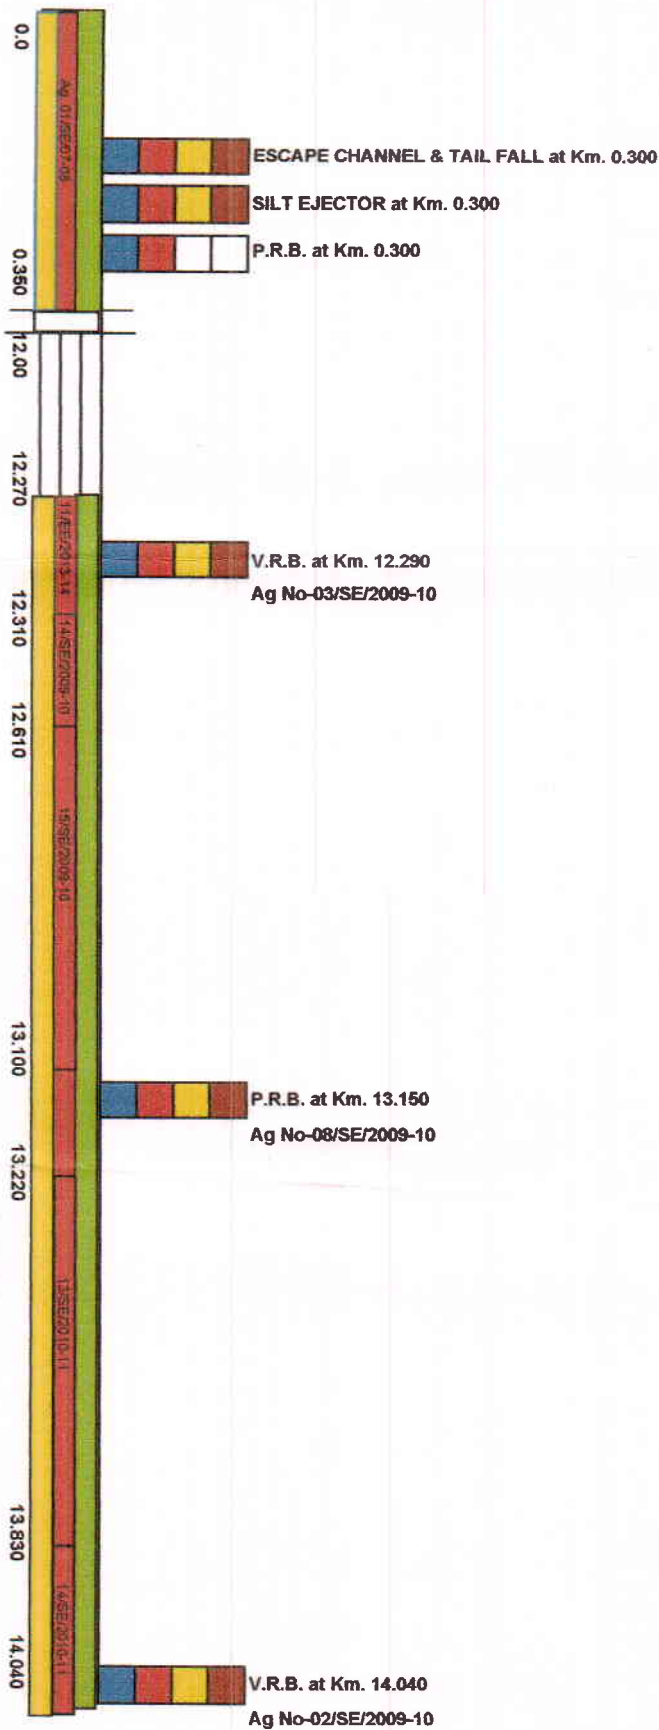

## LAND IN HECT.

| CHANGE                             | AREA OF LAND TO BEACQUIRED | AREA OF GOVT. LAND | LAND ACQUIRED UPTO LAST WEEK | AREA OF TOTAL LAND ACQUIRED UPTO 31.03.2016 | BALANCE LAND TO BEACQUIRED | TOTAL LAND  |
|------------------------------------|----------------------------|--------------------|------------------------------|---------------------------------------------|----------------------------|-------------|
| Km.0.00 to 0.350 & 12.00 to 14.040 | 30.00 hect.                | 2.00 hect.         | 29.008 hect.                 | 29.008 hect.                                | 00.992 hect.               | 30.00 hect. |

NOTE:-  
1- TOTAL LAND REQUIRED  
2- TOTAL LAND ACHIEVED  
3- BALANCE LAND TO BE ACQUIRED

Hect:-  
30.000  
29.008  
00.992

## Sl.No

## Details

## Colours


|   |                                                                                                   |           |
|---|---------------------------------------------------------------------------------------------------|-----------|
| 1 | Land progress through Negotiation 31.03.2016                                                      | 29.008 30 |
| 2 | Land Proposed through Negotiation up to 2015-2016                                                 | 0.350     |
| 3 | Canal Construction upto 31.03.2016                                                                | 29.008 30 |
| 4 | Canal Construction under progress                                                                 | 2.390     |
| 5 | Construction programme of puca work such as V.R.B. & P.R.B silt Ejector Tail Fall & Escapechannel |           |

Executive Engineer  
Madhya Ganga Canal Const. Div.-5  
Bijnor

Full Complete work  
Half work  
Agreement & Date of Start  
Drawing Estimate & Tender

**T-DIAGRAMME OF MADHYA GANGA CANAL CONSTRUCTION DIVISION-5, BINJOR ( STAGE-II )**  
**TAIL DY. FROM KM. 0.000 TO KM. 12.600 ( YEAR 2015-2016 )**

Progress up to 21.00.2016

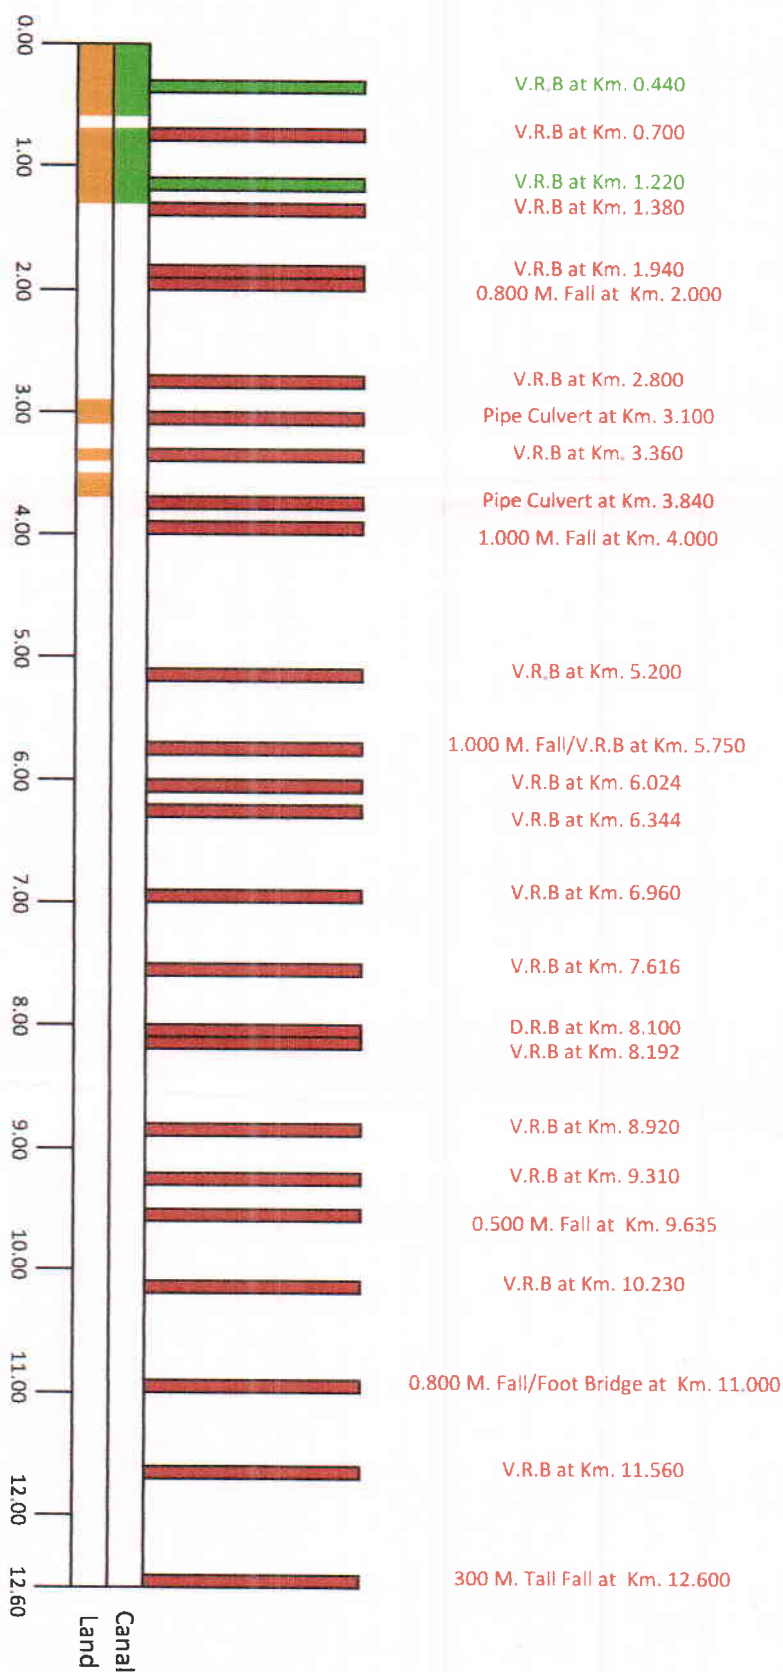

| LAND IN HECT.                   |        |
|---------------------------------|--------|
| Total:-                         | HECT   |
| 1:- TOTAL LAND REQUIRED         | 78.000 |
| 2:- TOTAL LAND ACHIEVED         | 3.654  |
| 3:- BALANCE LAND TO BE ACQUIRED | 74.346 |

| SI. NO. | DETAILS                        | COLOURS                                                                             |
|---------|--------------------------------|-------------------------------------------------------------------------------------|
| 1:-     | LAND ACQUIRED                  |  |
| 2:-     | LAND NOT ACQUIRED              |  |
| 3:-     | CANAL/ WORK COMPLETE           |  |
| 4:-     | BALANCE WORK AGAINST AGREEMENT |  |
| 5:-     | PROPOSED WORK                  |  |

Madhya Ganga Canal Const. Division-5

Executive Engineer

Binjor
